

RIG01 – Surface approach

15m rope, 2 hangers (alloy), Hilti anchors


RIG02 – Entrance pitch

Hilti anchors, alloy hangers preferred

-Rope 100m+20m

-17 Bolts

-2 Deviations

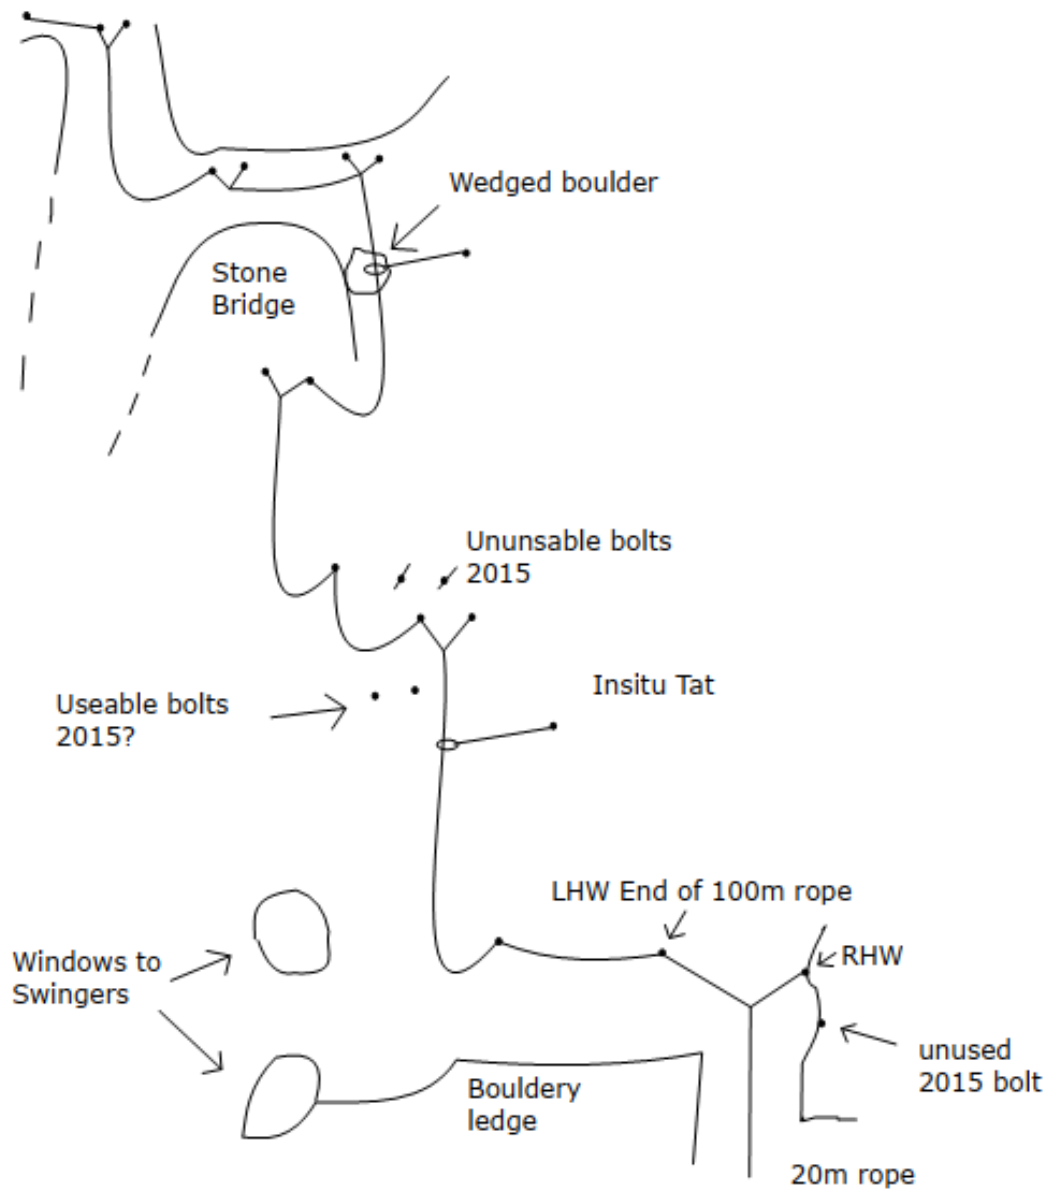

RIG02-01 – Slippy passage on approach to Natural Highs


20m rope, 1 sling + screwgate (from memory)

RIG05 – Pitch in Far Side

18m rope, 5 hangers (Hilti anchors, alloy hangers preferred)


From memory: traverse to y-hang, one rebelay, rope tied off on ledge

RIG06 – Honeycomb

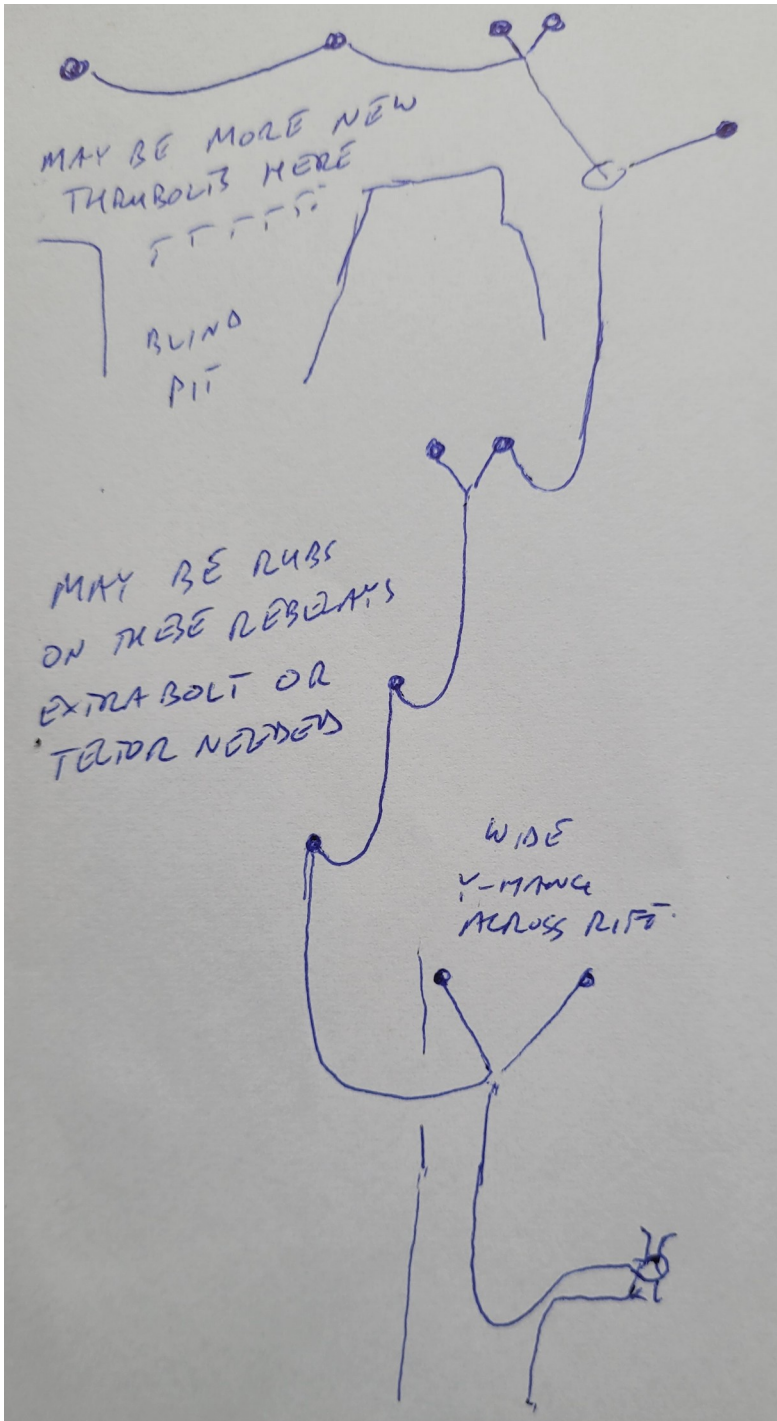

90m rope
11 hangers
Mostly Hiltis
Stainless preferred
1 sling + screwgate
1 deviation + snaplink

RIG07 – Short pitch after Honeycomb

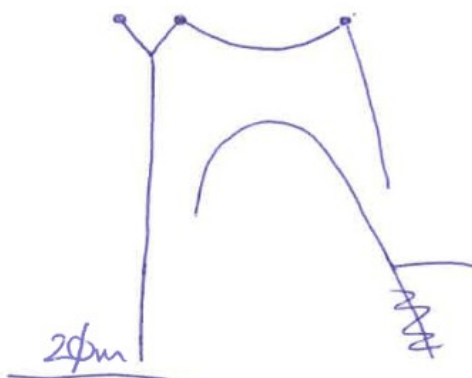


20m rope
3 hangers
Thurbolts
Stainless preferred

RIG08 – Climb up and down to approach Hangmans

25m rope, 2 hangers (Hilti anchors, stainless hangers preferred), 2 sling + screwgate

From memory: One or two Hiltis at top of climb, one or two naturals lower down on the Hangmans side.

RIG09 – Hangman's pitch

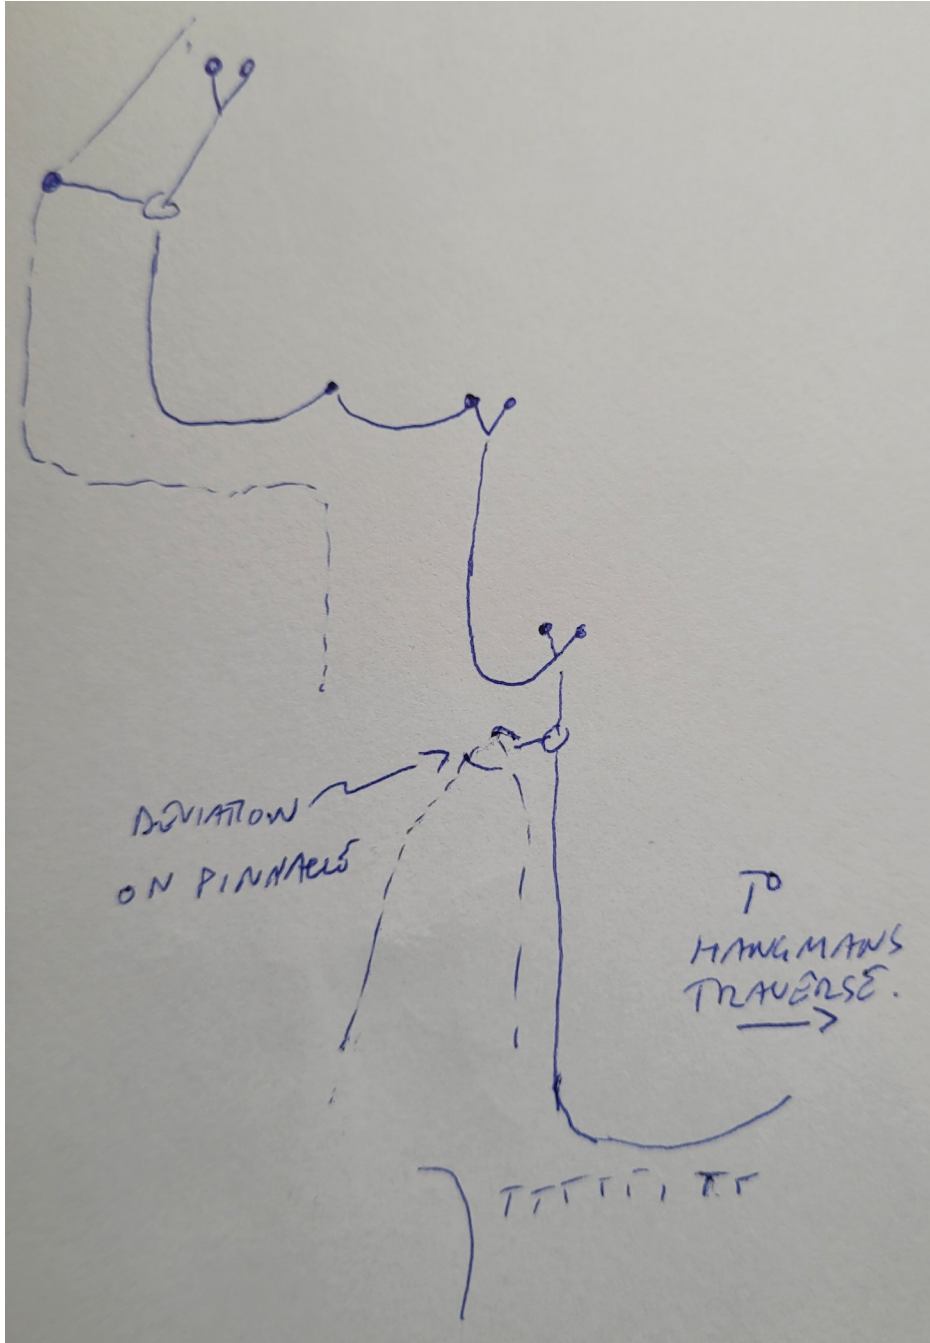

65m rope

8 hangers

6 Hiltis

2 ThruBolts

Stainless preferred

2 deviations


DEVIATION
ON PINNACLES

TO
HANGMAN'S
TRAVERSE.
→

TTTTTTT

RIG10 – Hangman's traverse + climb up at end

40m rope, 4 hangers (Hiltis, stainless preferred), 1 sling + screwgate

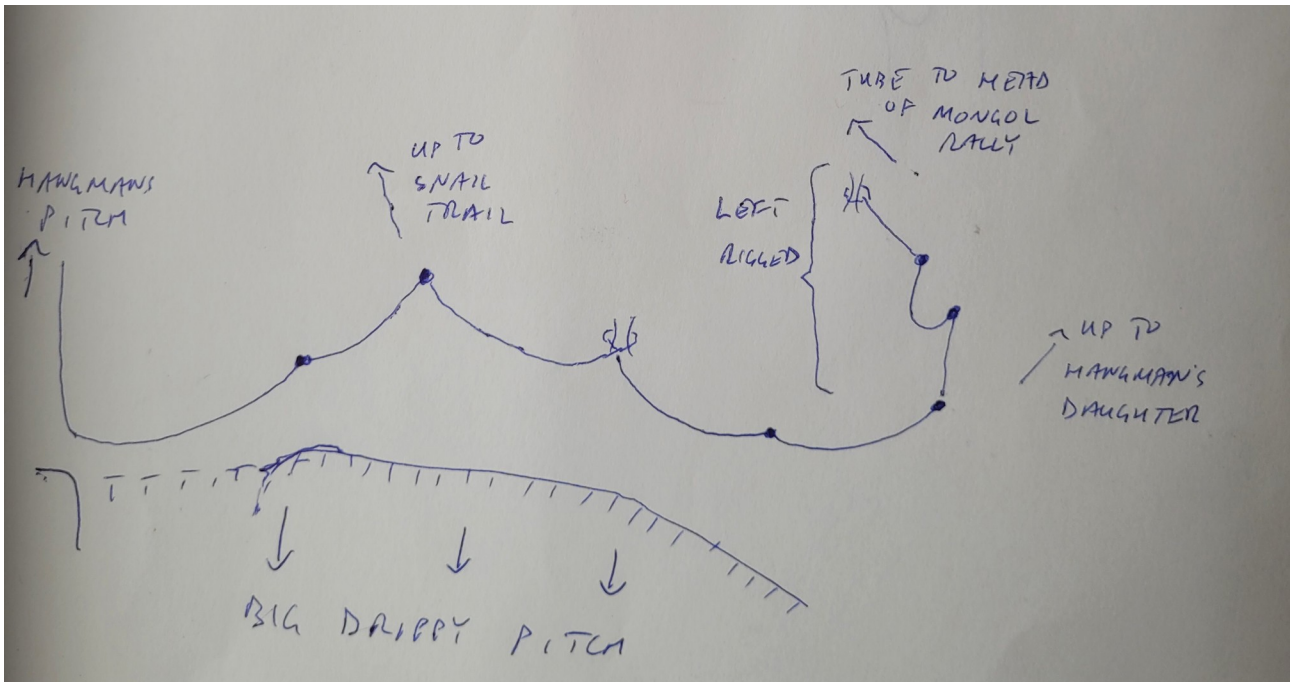

RIG11 – Short pitch and traverse to head of Mongol Rally


23m rope, 3 hangers (Hiltis, alloy preferred), 1 sling + screwgate

RIG12 – Mongol Rally to Pit Stop

202m rope, 21 hangers (Hiltis, alloy preferred), 1 sling + screwgate, 2 deviations


Would benefit from a few additional bolts.

Suggest we take a new 200m reel (which will be ~180m in reality) and an additional ~50m rope. Join at a convenient anchor to avoid knot passes.

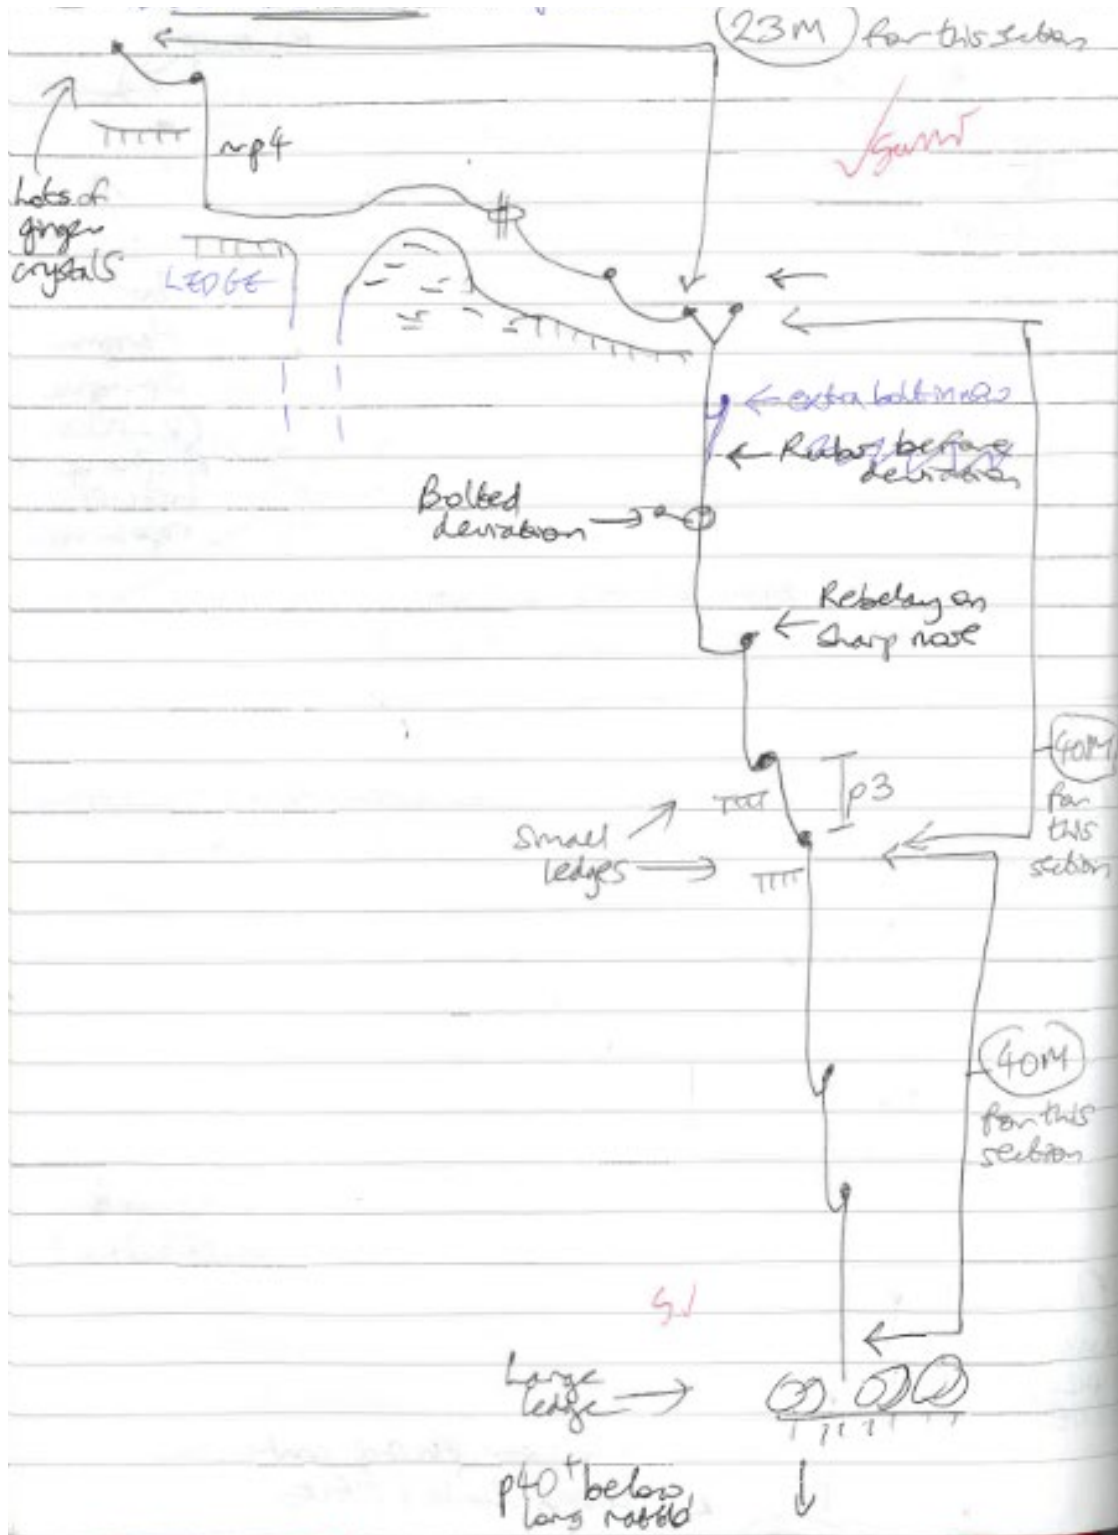


...continues over

Mongol Rally to Pit Stop continued

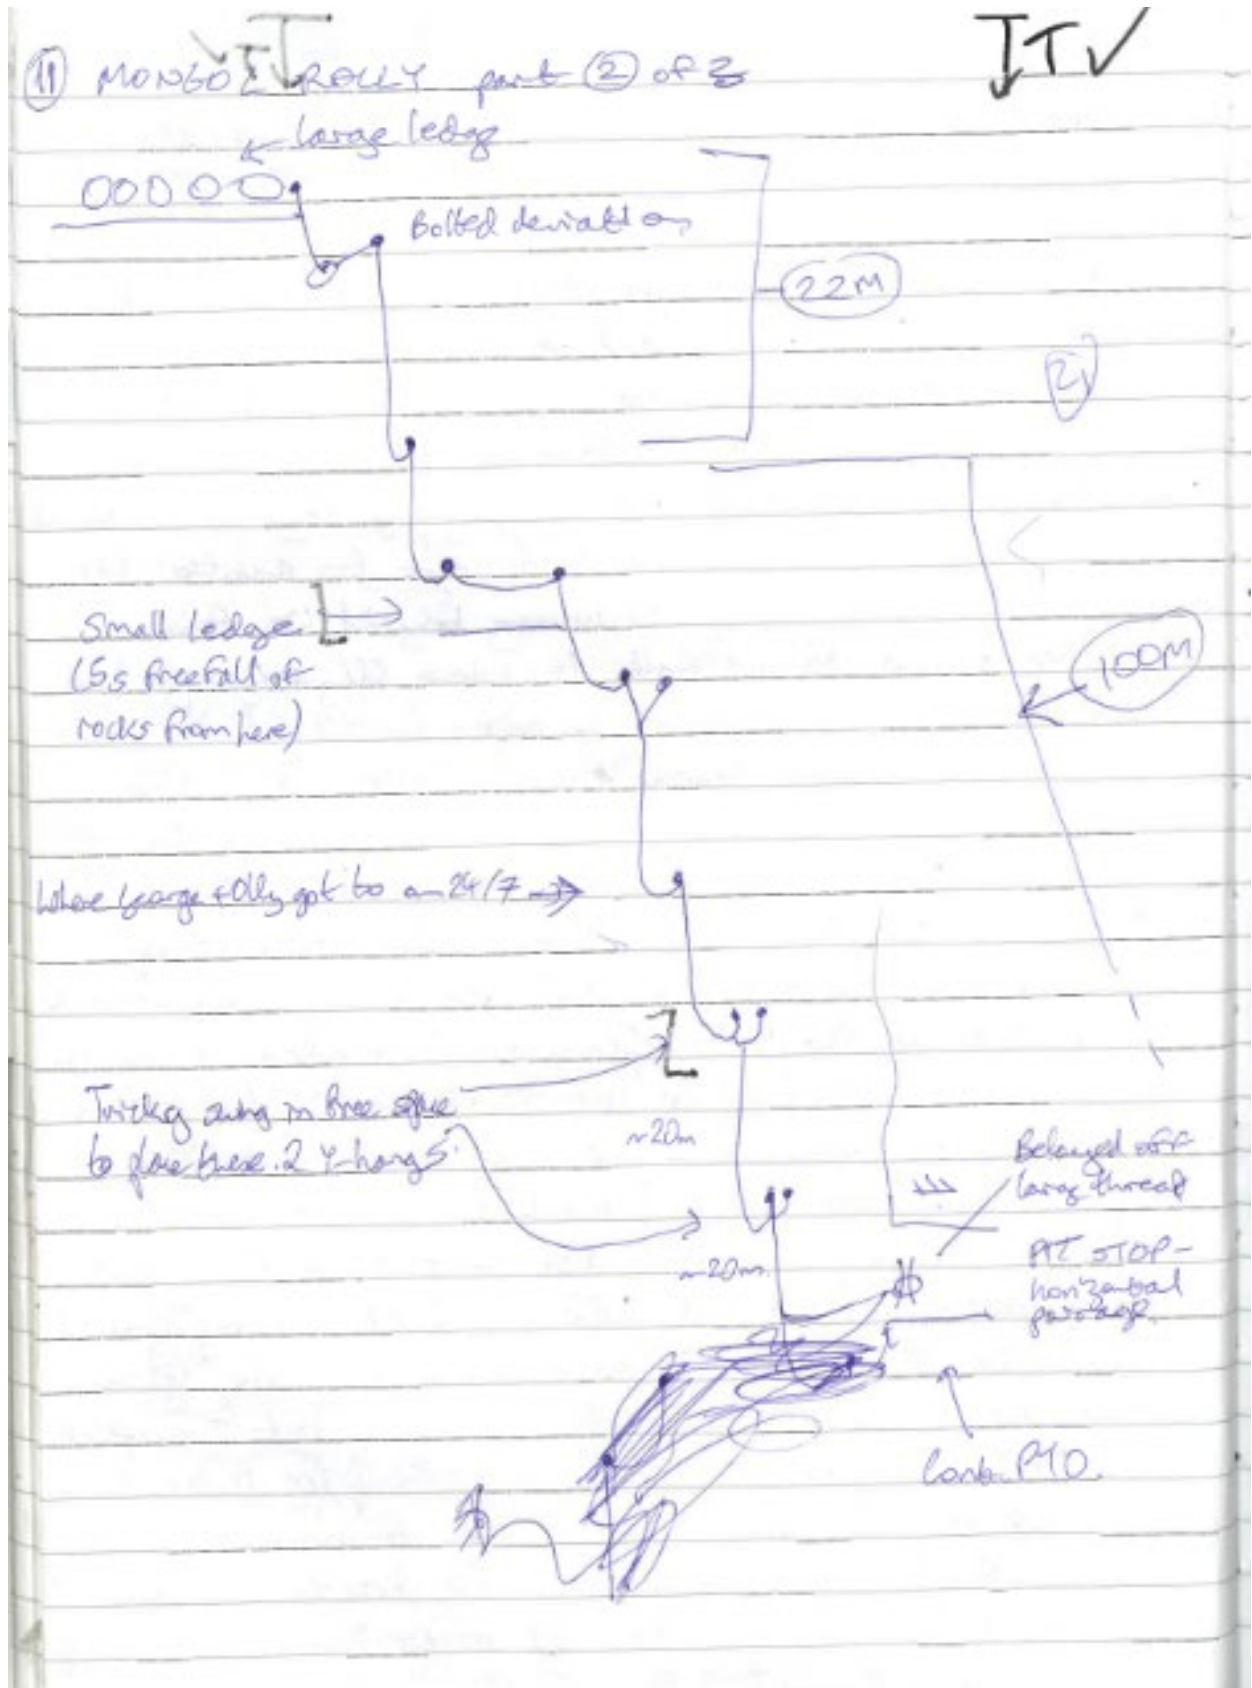

RIG12-05 – Pitch in Northern Pit Stop

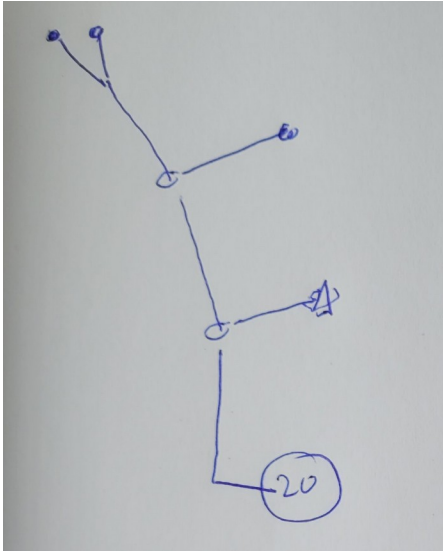

20m rope
3 hangers
Thrubolts
Stainless preferred
2 deviation + snaplink

RIG12-06 – Pitch up into Northern Powerhouse

Left rigged, but rope condition needs checking. Would benefit from rebolting


RIG16 – Handline in Erechtheion

Allow 10m rope, 2 hangers (thrubolts)

Gear requirement is a complete guess. No mention of bolts in logbook – provision made in case some were placed

THIS PAGE INTENTIONALLY LEFT BLANK

RIG17 – Tartarus

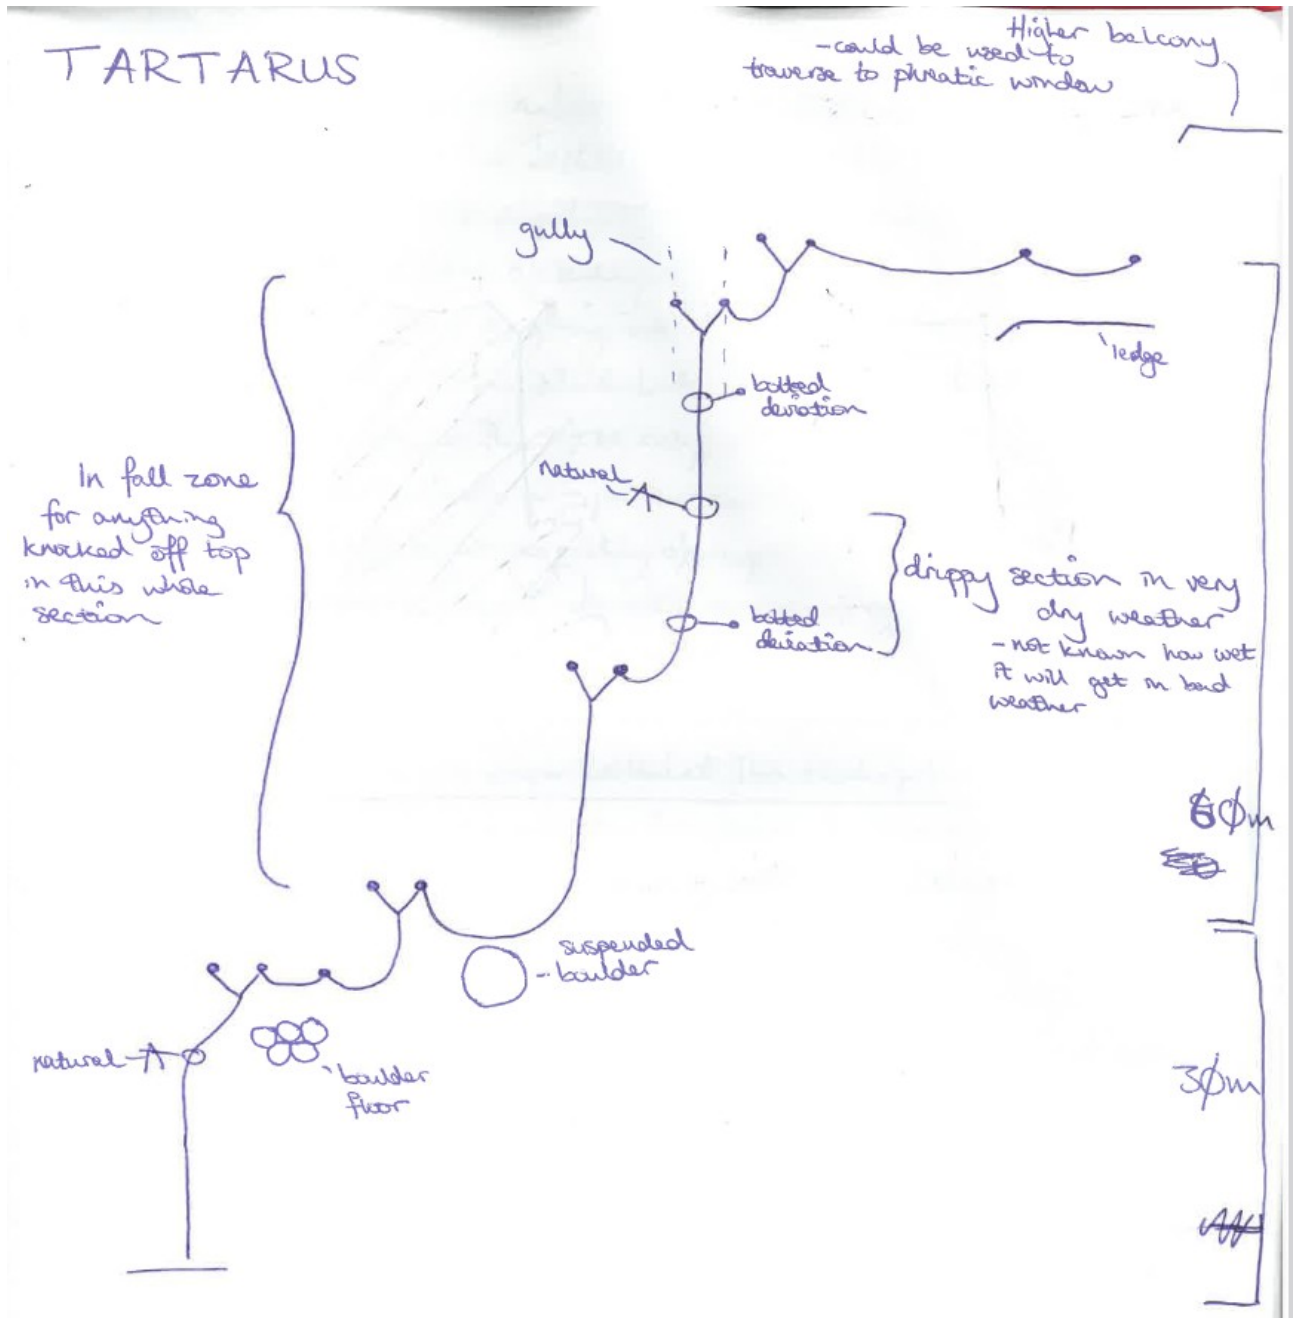

90m rope (left in cave end 2022)


15 hangers

Thrubolts

Alloy preferred


4 deviations + snaplinks

RIG18 – Short pitch below Tartarus

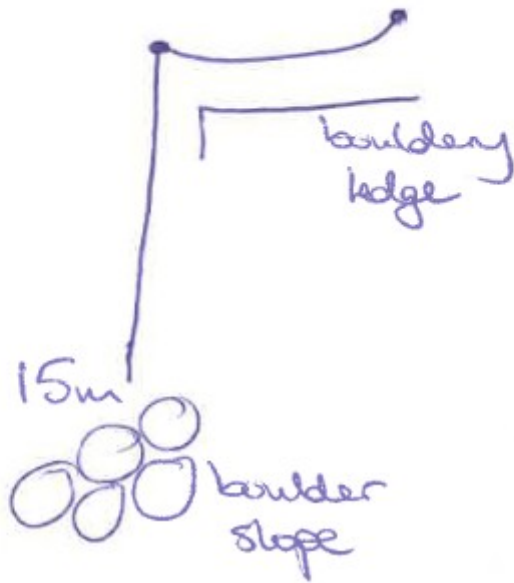

15m rope (left in cave end 2022)
2 hangers
Thrubolts
Alloy preferred

RIG19 – Muddy slope at start of Ichthyas

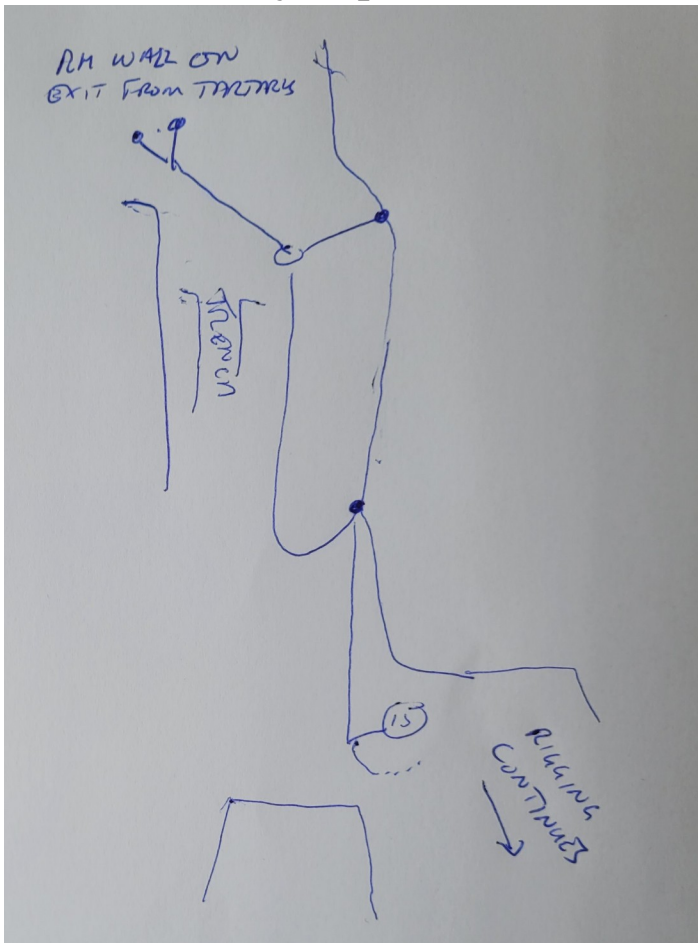

15m rope
4 hangers
Thrubolts
1 deviation + snaplink

Rigging continues after this pitch
(no documentation found)
